

Lincolnshire Broadband Programme


Programme Status

Lincolnshire Broadband Programme

- Overview
- Objectives
- Funding
- Current Status
- The Future


Lincolnshire Broadband Programme

- *Overview*
 - Covers 156,667 Business & Residential premises deemed eligible under State Aid
 - Completion date is April 2016
 - Project split into 8 phases of work
 - BT are delivering the Implementation under the BDUK Framework Agreement

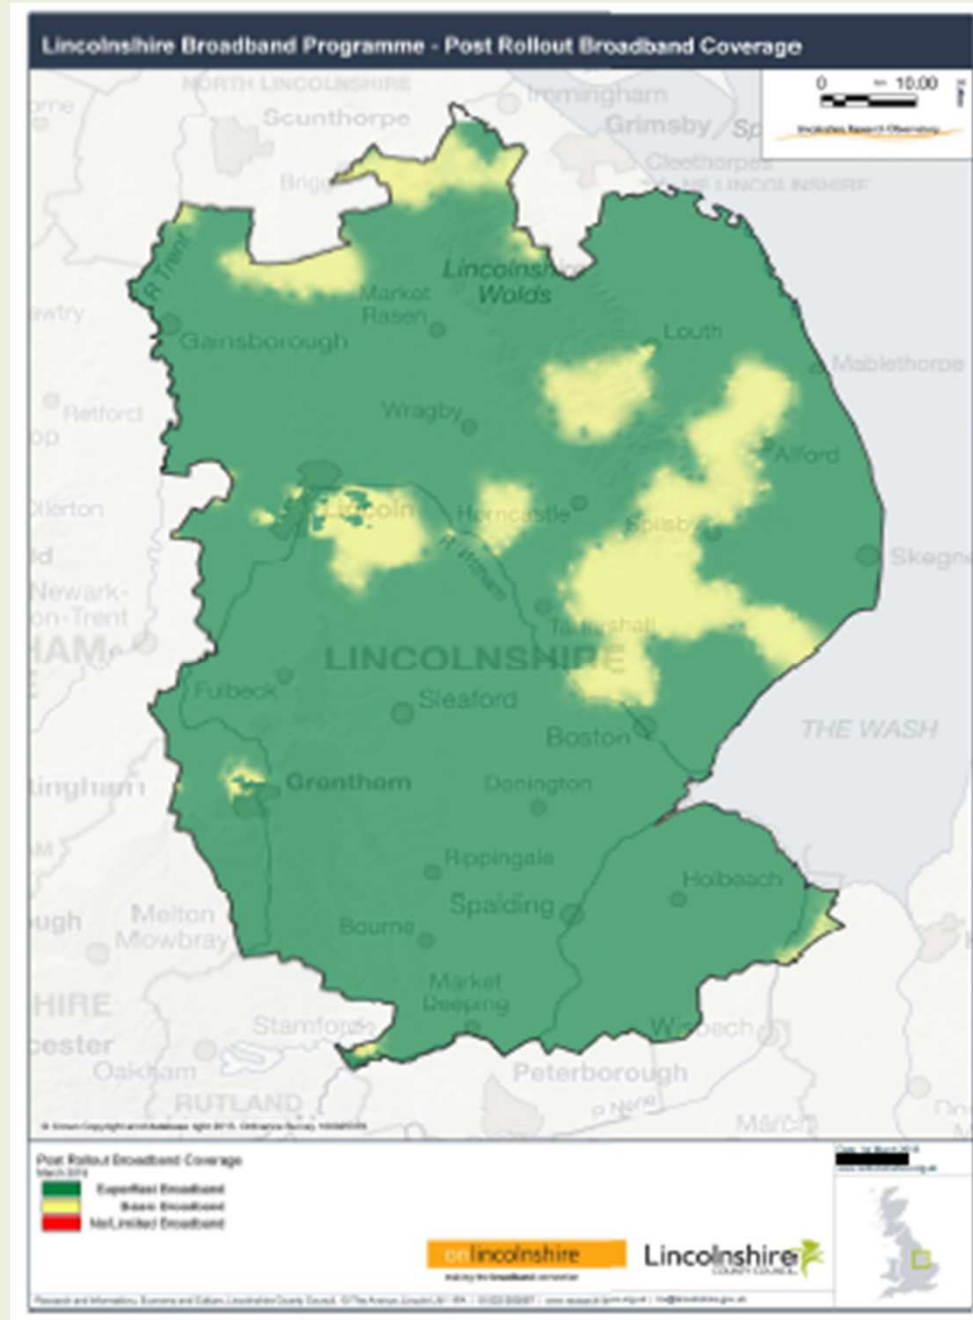

Lincolnshire Broadband Programme

- *Overview (Cont)*
 - ERDF Funded (£300K) Fixed Wireless Project delivered in East of county by Lincolnshire company AB Internet
 - Original Intervention Area was circa 4.5K Premises
 - Actual coverage achieved is circa £12.5K
 - Provides up to 100Mb/s download speeds

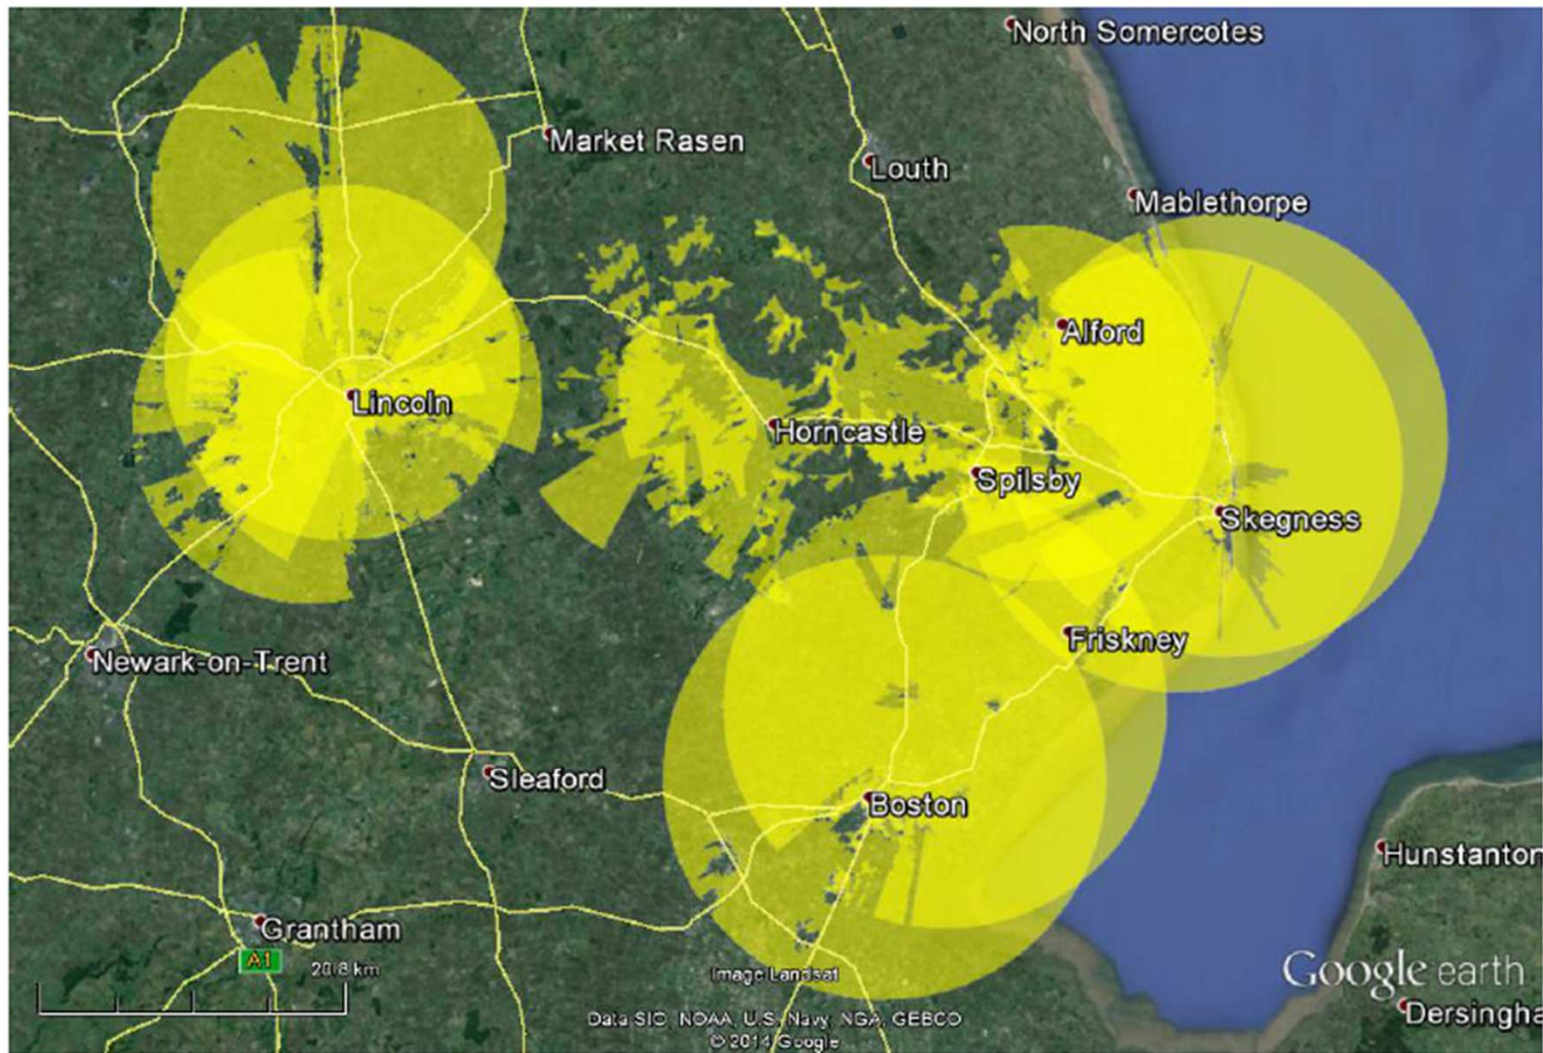

Google earth



Lincolnshire Broadband Programme

- *Objectives*
 - Provide Superfast Broadband (>24Mb/s Download) to 90% of Lincolnshire premises
 - Provide a minimum of 2Mb/s Download to 100% of Lincolnshire premises
 - ERDF Funding to provide infrastructure to eligible SMEs

Lincolnshire Broadband Programme

➤ *Funding*

- £14.31 BDUK
- £10M LCC
- £4M Districts
- £1.6M ERDF
- £510K LCC (Gap fund to ERDF)
- BT £10M

- Total £40.4M

Lincolnshire Broadband Programme

➤ *Current Status*

- 58,900 Premises Passed
- 242 BT Cabinets complete
- Currently working Phases 3 & 4
- Cabinets completed in all 7 Districts
- Fixed Wireless Project now complete and operational

Lincolnshire Broadband Programme

➤ *The Future*

- Additional BDUK Funding of £2.35M granted to Lincolnshire
- LCC has added a further £1.8M with additional EU money currently being sourced
- Target delivery is 95% Superfast coverage by 2017
- LCC are now looking at how best to utilise this funding

onlincolnshire

making the **broadband** connection

Lincolnshire Broadband Programme

Thank You For your Time Today

This page is intentionally left blank
