

Lincolnshire Broadband Programme

Phase 2 Deployment:



Bringing it all together



**SUPERFAST
BRITAIN**



making the **broadband** connection

Lincolnshire Broadband Programme

- Current Status
- Funding Position
- Numbers of Premises Involved
- Timescales
- The Future

Lincolnshire Broadband Programme

Current Status

At 31st March 2016 we had achieved 90% Superfast coverage

At 31st July 2017 157K premises were fibre enabled


Phase 2 now extends to December 2019

Phase 2 originally 7K premises - now 21K Premises

Page 3

Lincolnshire Broadband Programme


Funding - Phase 2

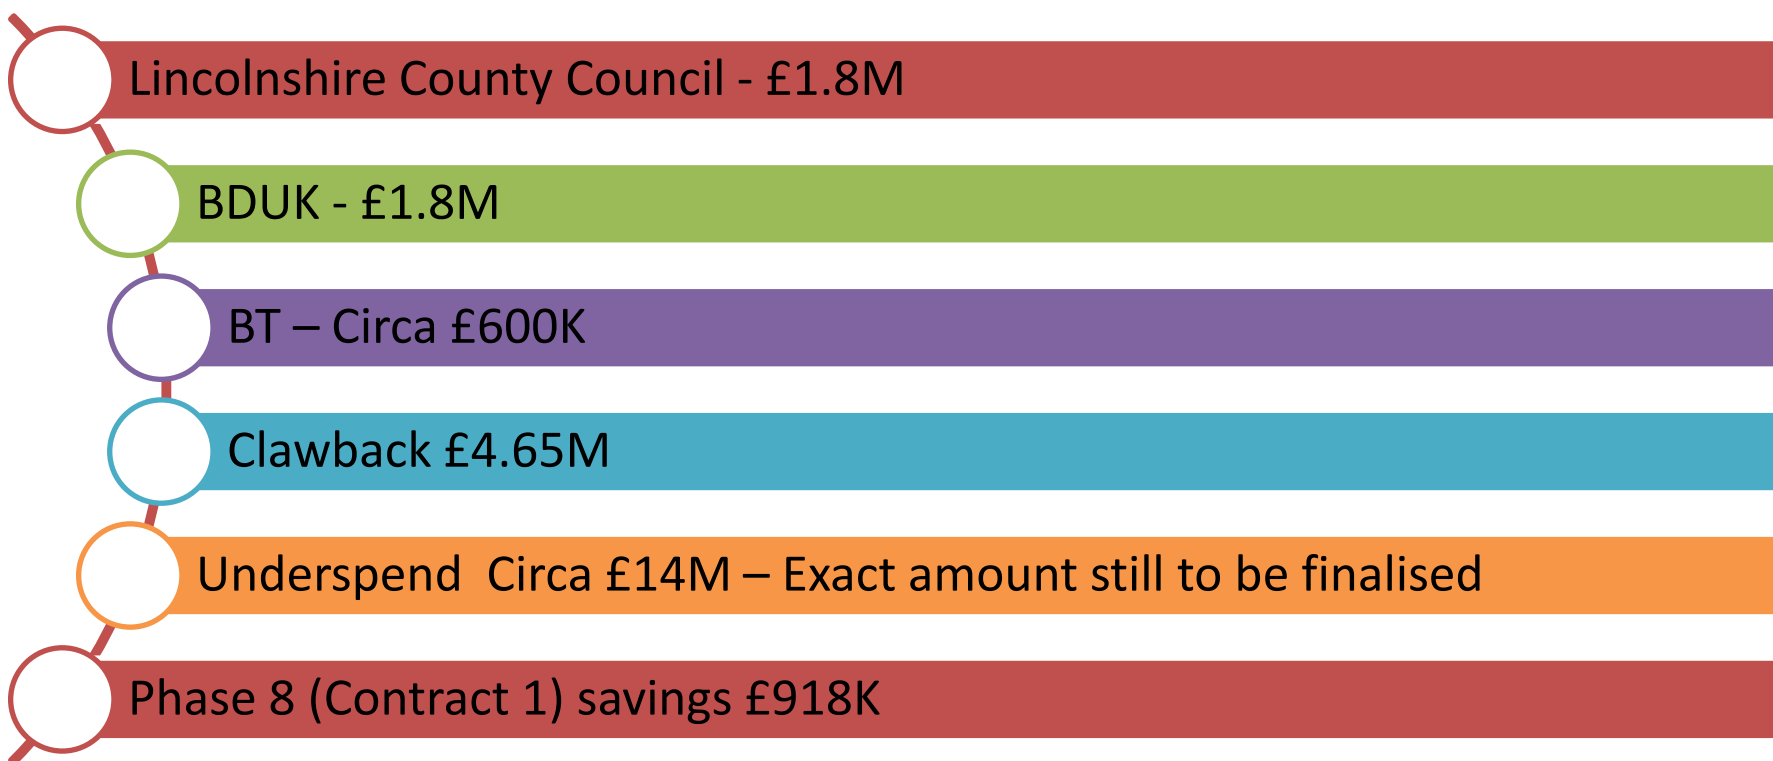

Page 4

Lincolnshire Broadband Programme

Planned Premises Enabled – Phase 2

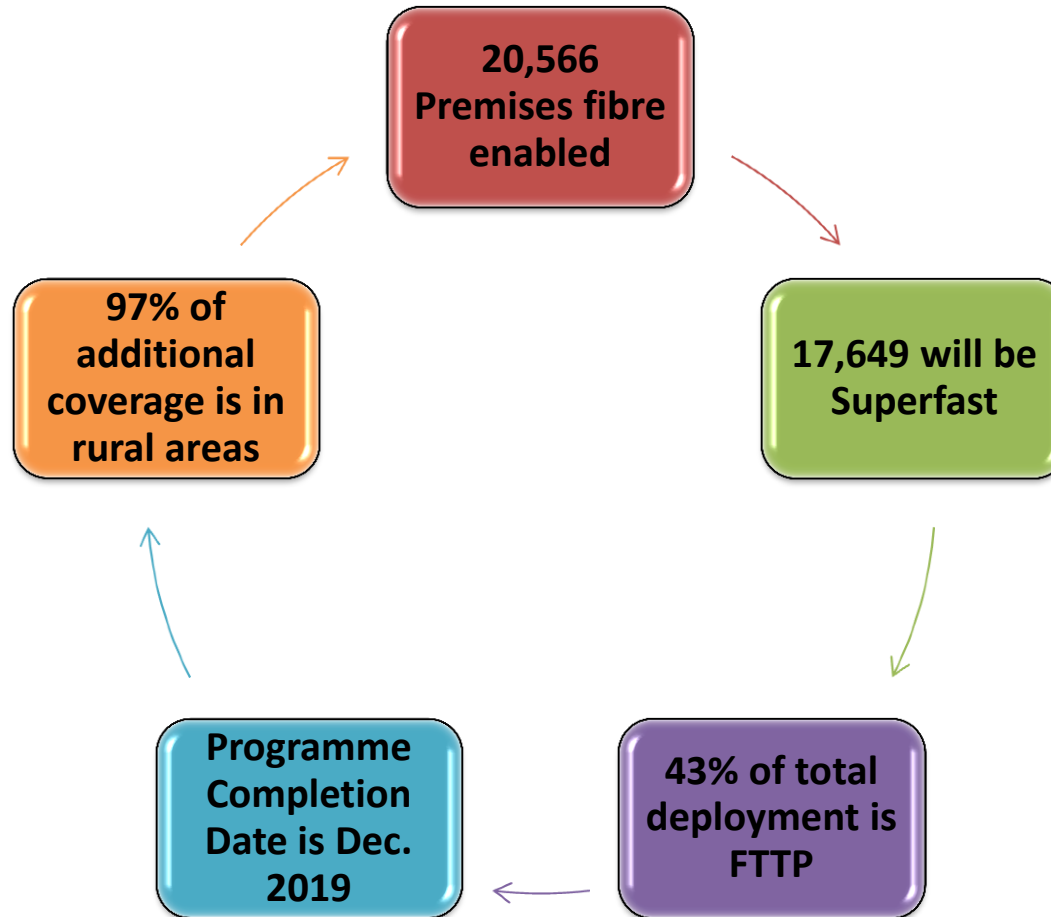

Lincolnshire Broadband Programme

Timescales


Phase 2 build was due to end 30th September 2017

The Implementation Plan for new Phase 2 gives a build completion Q3 2019-20, but we believe it will complete sooner

Any additional Change Requests (CRs) will be merged into these timescales. This includes the latest 2 x CR which provides an additional 3700 Superfast Premises

We are still looking at viable areas, but these are getting fewer

Lincolnshire Broadband Programme

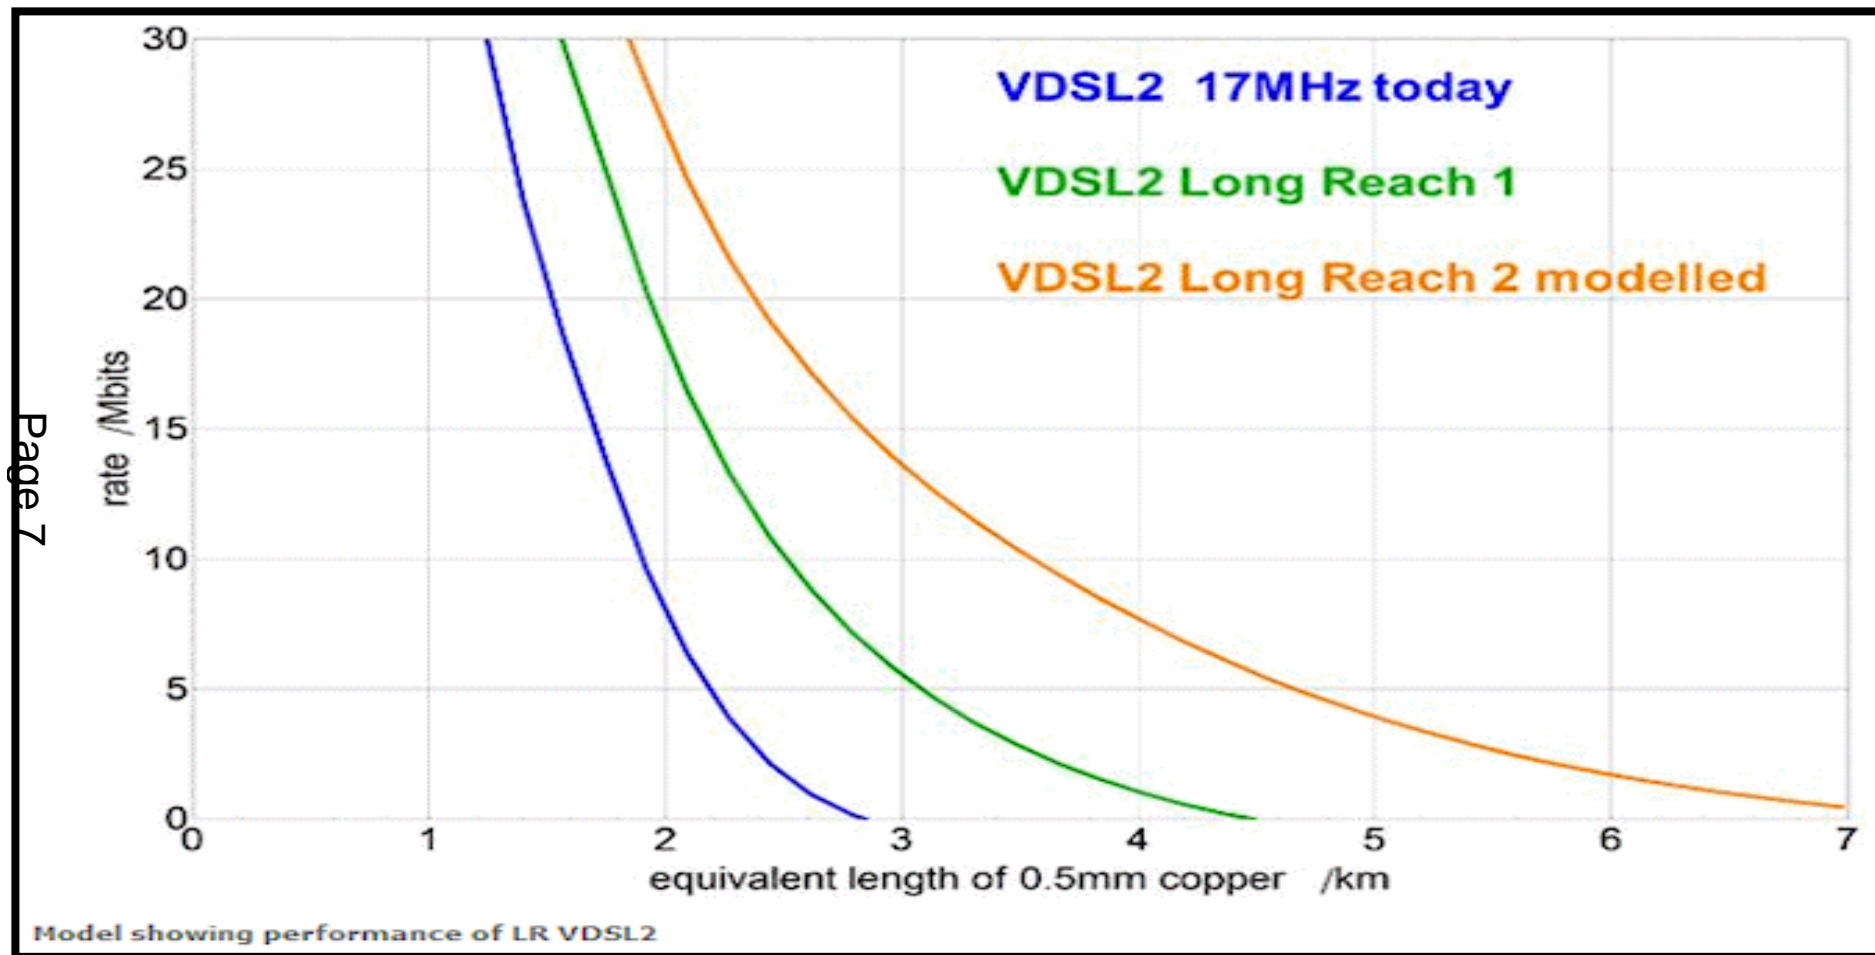

Lincolnshire Broadband Programme

The Future

- Phase 2 will push county-wide coverage to circa 97% with existing CRs pushing Phase 2 total to 24.5K fibre enabled premises
- There will still be around 10.5K premises without and we are considering possible options to cover them within existing timescales. We are currently running 4G trials at some sites
- The Local Full Fibre Networks scheme is ongoing and Districts have been asked for input. We have submitted an Expression of Interest

Lincolnshire Broadband Programme

The Future (Cont.)

- Seeking additional ERDF funding to improve SME connectivity
- Considering the use of 'Street Furniture' as a method of alternative deployment e.g Fixed Wireless, 4G, 5G
- We believe that the arrival of 5G will provide many of the missing answers to parts of the county and we could look at how to incentivise providers in Lincolnshire

Lincolnshire Broadband Programme

Any Questions?

The New Economic Infrastructure Strategy

**A Commissioned Programme Of
Activity By The Enterprise
Commissioner**

Purpose of Strategy

- To provide an evidence based rationale for LCC involvement in new Economic infrastructure provision

Commissioning Objectives


Sustaining And Growing Business And The Economy By

- Investing in sites where the market is failing to invest speculatively.
- Providing locations for important businesses to grow.
- Accelerating investment where conditions are positive.

What Parts Of Lincolnshire Have Greatest Demand For Employment Land




Where Does Lincolnshire Have Serviced Land Available?

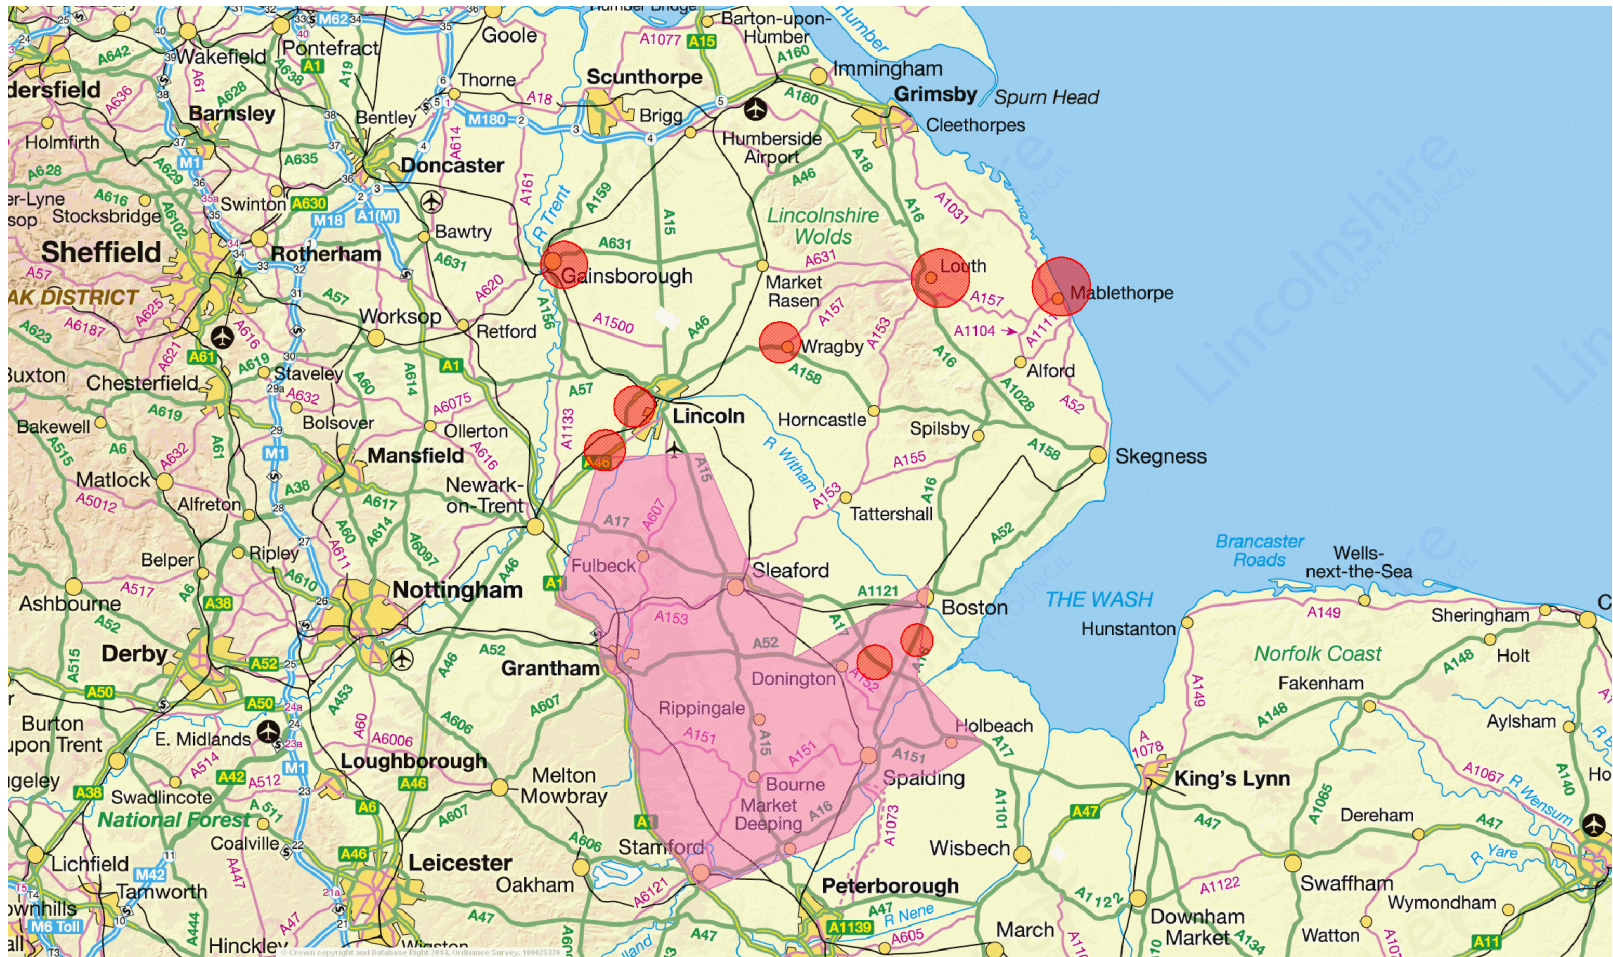

How Does Demand For And Availability Of Employment Sites Correlate With Our FDI Clusters

Page 16

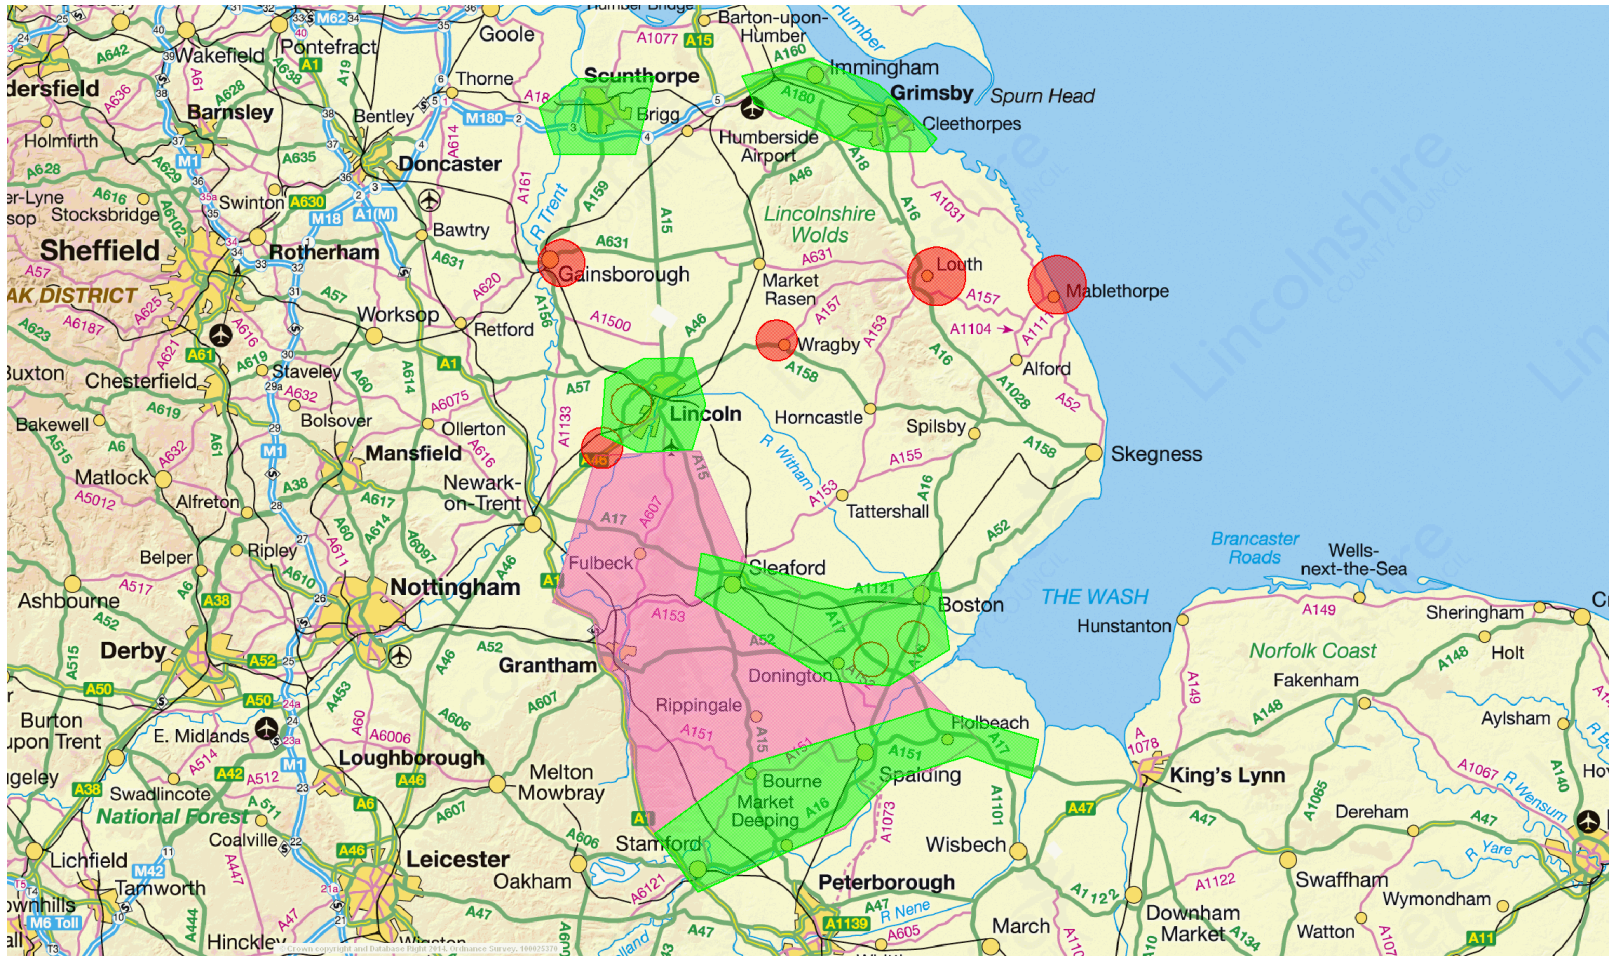

Hotel Requirements



Demand For Business Premises



Summation

- Lack of available business premises along coast, across south Lincolnshire and around Gainsborough.
- Shortage of serviced employment land ready for occupation in south east of Lincolnshire
- Hotels required in Grantham, Boston, Holbeach, Lincoln and Sleaford

Project Proposals

This map plots the locations in which projects in the commission activity plan will be delivered, some locations may have more than one project

