

onlincolnshire

making the **broadband** connection

# Lincolnshire Broadband Programme

Programme Status


## Lincolnshire Broadband Programme

- Overview
- Objectives
- Funding
- Current Status
- The Future

## Lincolnshire Broadband Programme


- *Overview*
  - Covers 156,667 Business & Residential premises deemed eligible under State Aid
  - Completion date is April 2016
  - Project split into 8 phases of work
  - BT are delivering the Implementation under the BDUK Framework Agreement

### Lincolnshire Broadband Programme - Post Rollout Broadband Coverage

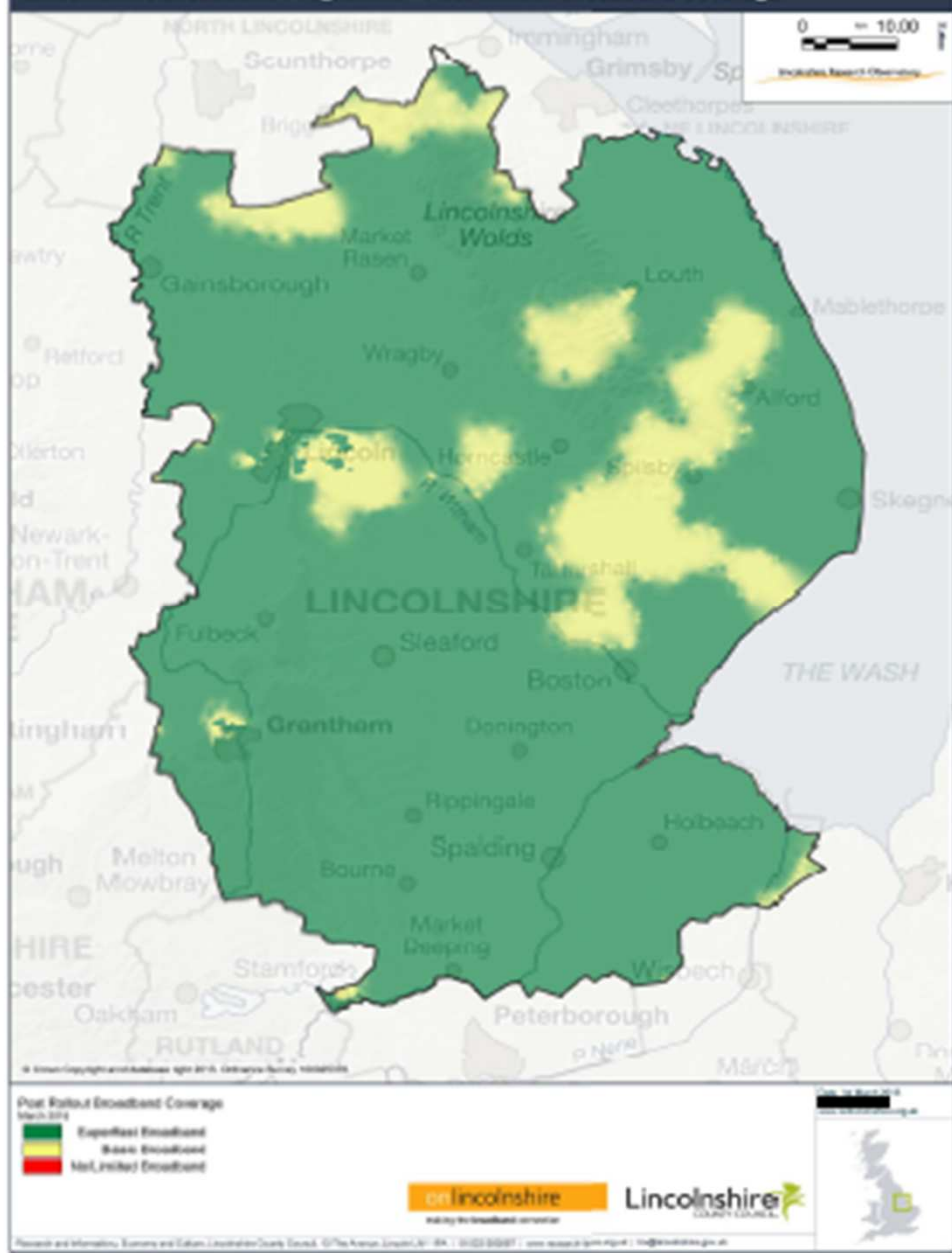

## Lincolnshire Broadband Programme

- *Overview (Cont)*
  - ERDF Funded (£300K) Fixed Wireless Project delivered in East of county by Lincolnshire company AB Internet
  - Original Intervention Area was circa 4.5K Premises
  - Actual coverage achieved is circa £12.5K
  - Provides up to 100Mb/s download speeds

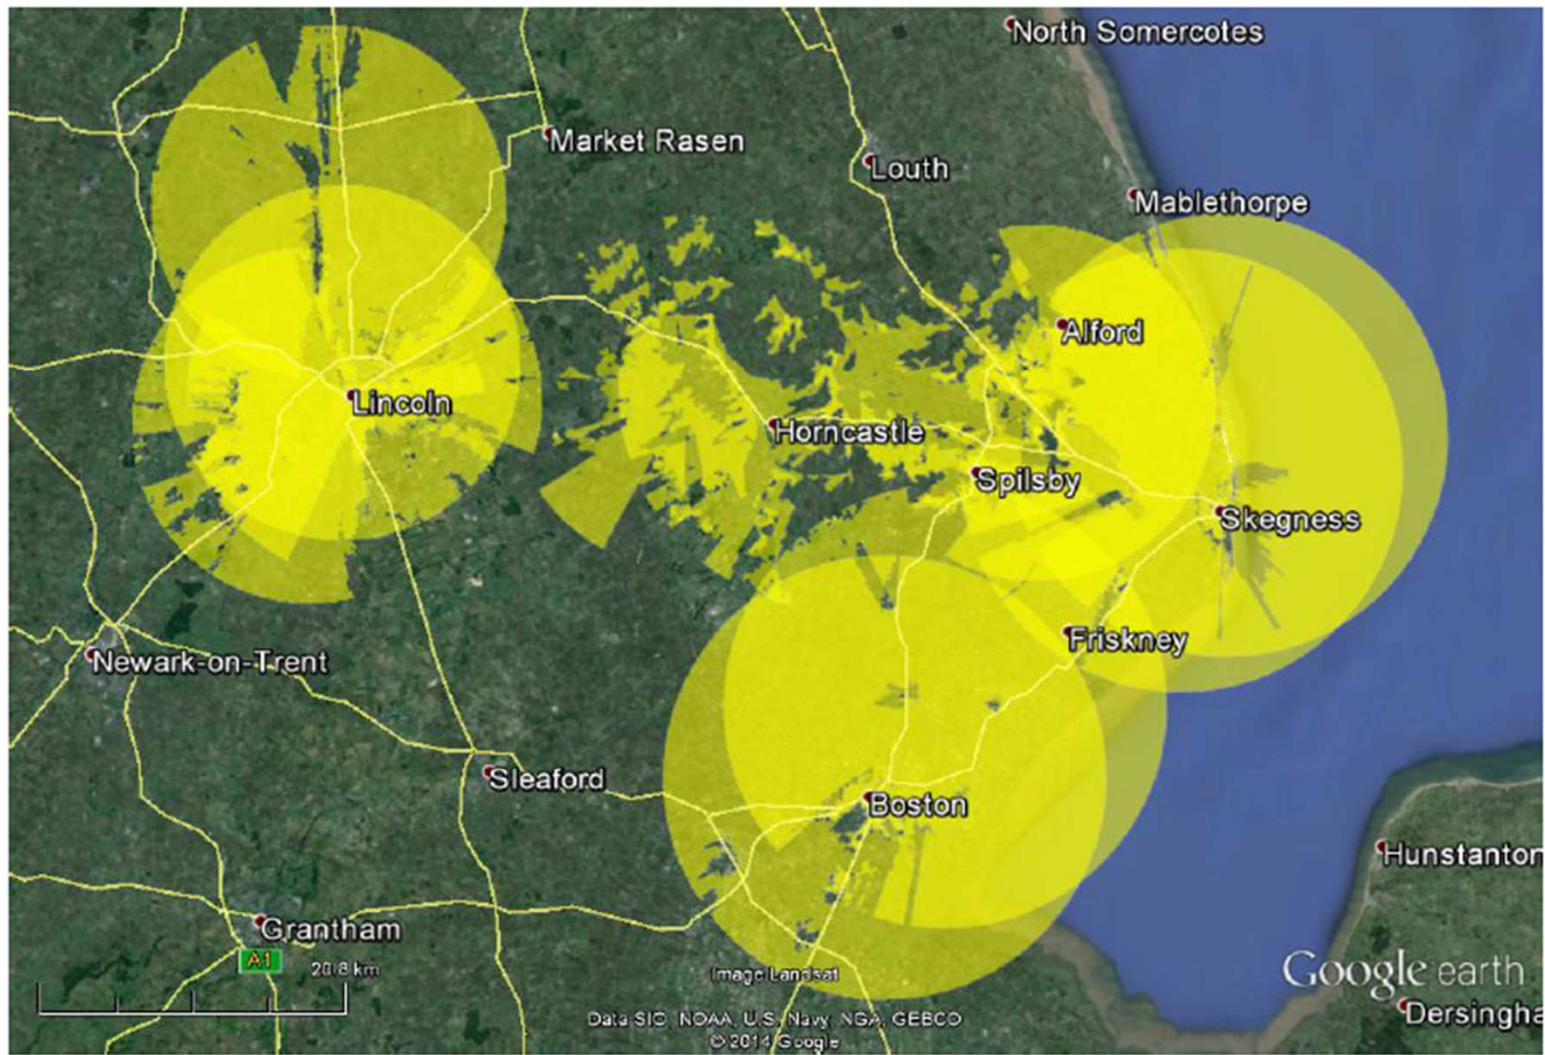

Google earth

miles  
km



## Lincolnshire Broadband Programme

- *Objectives*
  - Provide Superfast Broadband (>24Mb/s Download) to 90% of Lincolnshire premises
  - Provide a minimum of 2Mb/s Download to 100% of Lincolnshire premises
  - ERDF Funding to provide infrastructure to eligible SMEs

## Lincolnshire Broadband Programme

### ➤ *Funding*

- £14.31 BDUK
- £10M LCC
- £4M Districts
- £1.6M ERDF
- £510K LCC (Gap fund to ERDF)
- BT £10M
  
- Total £40.4M



## Lincolnshire Broadband Programme

### ➤ *Current Status*

- 58,900 Premises Passed
- 242 BT Cabinets complete
- Currently working Phases 3 & 4
- Cabinets completed in all 7 Districts
- Fixed Wireless Project now complete and operational

## Lincolnshire Broadband Programme

- *The Future*
  - Additional BDUK Funding of £2.35M granted to Lincolnshire
  - LCC has added a further £1.8M with additional EU money currently being sourced
  - Target delivery is 95% Superfast coverage by 2017
  - LCC are now looking at how best to utilise this funding

onlincolnshire

making the **broadband** connection

Lincolnshire Broadband Programme

Thank You For your Time Today
